

SUPPLY SCOPE (distributor quantities, no material prices): Nudura ICF walls above the basement, pre-cut by BuildEase - LG 457 core (unassembled XR35 panels on insert webs + 4-way connectors, corners lapped straights, openings timber-bucked by others) and 8in Std internal walls on the transfer deck, GF / FF external walls in 6in XR35. The raft, existing basement, decks, slabs, steels, roof, windows, doors and partitions are shown in good faith only (design assumptions) - engineer / specialists to design.

QUOTATION - NOT FOR CONSTRUCTION

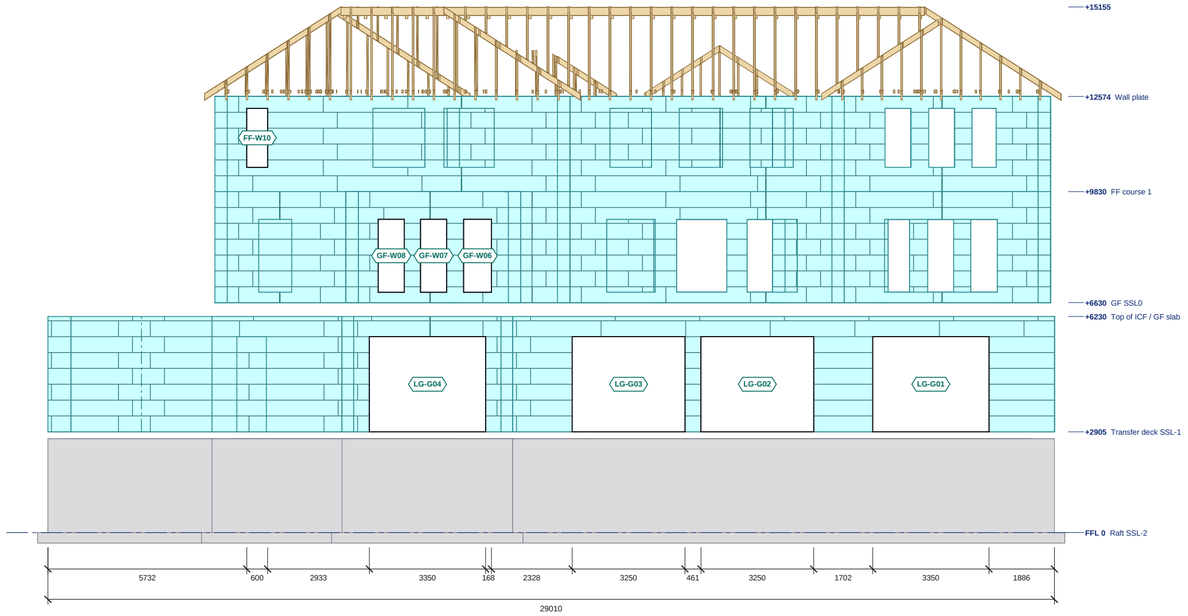

NORTH ELEVATION

Scale 1:125 @ A2 | Levels above GF FFL; sills and heads in the schedule

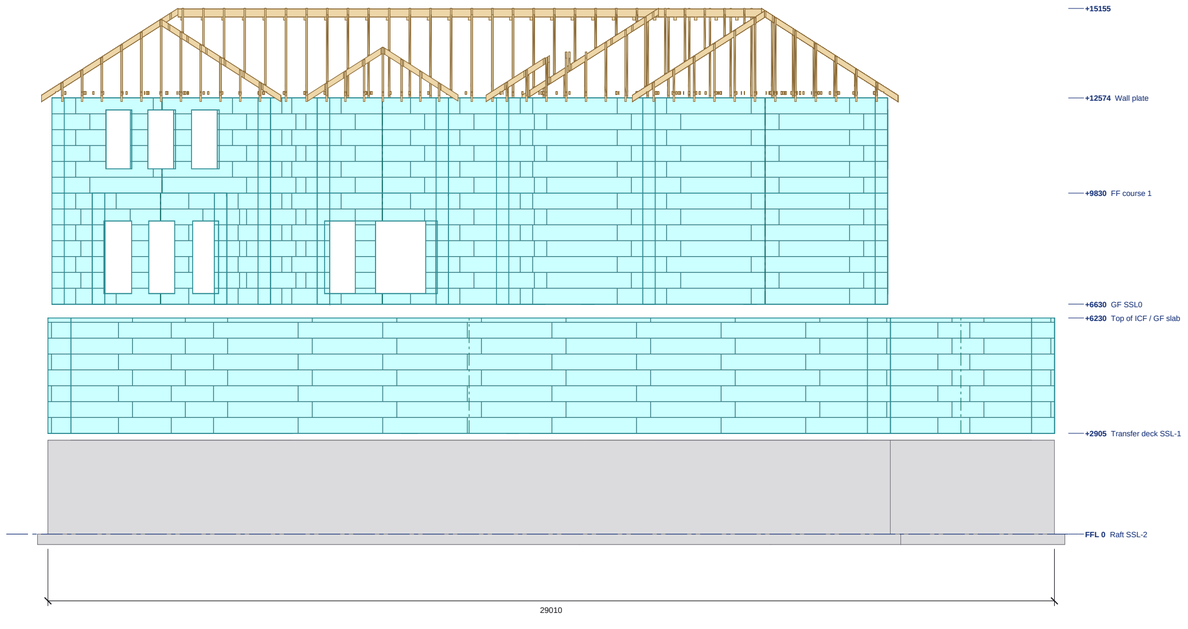

SOUTH ELEVATION

Scale 1:125 @ A2 | Levels above GF FFL; sills and heads in the schedule

ICF external EPS face
Block course joint
Stack joint

0 1 2 3 4 5m

ELEVATION SCHEDULES

NORTH ELEVATION: OPENINGS

Ref	Width	Height	Sill	Head	Lintel
FF-W10	600	1700	+10530	+12230	-
GF-W06	800	2100	+6930	+9030	-
GF-W07	750	2100	+6930	+9030	-
GF-W08	750	2100	+6930	+9030	-
LG-G01	3350	2743	+2905	+5648	-
LG-G02	3250	2743	+2905	+5648	-
LG-G03	3250	2743	+2905	+5648	-
LG-G04	3350	2743	+2905	+5648	-

Structural openings in the ICF; sill and head above GF FFL.

SOUTH ELEVATION: OPENINGS

Ref	Width	Height	Sill	Head	Lintel
none					

Structural openings in the ICF; sill and head above GF FFL.

NORTH ELEVATION: LEVELS

Level	FFL
Raft SSL-2	0
Transfer deck SSL-1	+2905
Top of ICF / GF slab	+6230
GF SSL0	+6630
FF course 1	+9830
Wall plate	+12574
top of roof build-up	+15155

SOUTH ELEVATION: LEVELS

Level	FFL
Raft SSL-2	0
Transfer deck SSL-1	+2905
Top of ICF / GF slab	+6230
GF SSL0	+6630
FF course 1	+9830
Wall plate	+12574
top of roof build-up	+15155

NOTES

1. ICF: Nudura 6" XR35, 101.6 EPS + 152.4 core + 101.6 EPS = 355.6; 9.18in XR35 Panel Series, 101.6 EPS + 457.2 core + 101.6 EPS = 660.4; 8" Std, 66.7 EPS + 203.2 core + 66.7 EPS = 336.6. External EPS face shown with the block course joints, vertical block joints and stack joints as populated.
2. Levels above GF FFL. Openings are structural openings in the ICF; glazing, doors, render and finishes by others, not shown.
3. ICF walls as modelled.
4. See ES26-088-GA-01 for plan setting out, lintels and steel.
5. Datum: 0 = raft SSL-2 (+40.357). Transfer deck SSL-1 +43.262, Top of ICF +46.587, GF SSL0 +46.987, FF SSL1 +50.297, U/S wall plate +52.962.
6. From BDI 20164022 S1 02 / S3 02 (C4), the architect's GF / FF plans and Ethos' extension sketch.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
Ethos Property Developments (Nudura distributor) - Mark Whalley	House - walls above the basement, Badgers Hollow, Alderley Edge

DRAWING TITLE
FRONT AND REAR ELEVATIONS

ICF elevations with openings, levels and roof build-up

SCALE	SIZE	DATE
1:125	A2	02.11.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-088-EL-01	-

Do not scale. All dimensions in millimetres, levels in metres from GF FFL. Check all dimensions on site.
